Sunnyvale Cleanwater Program
Project Sequencing
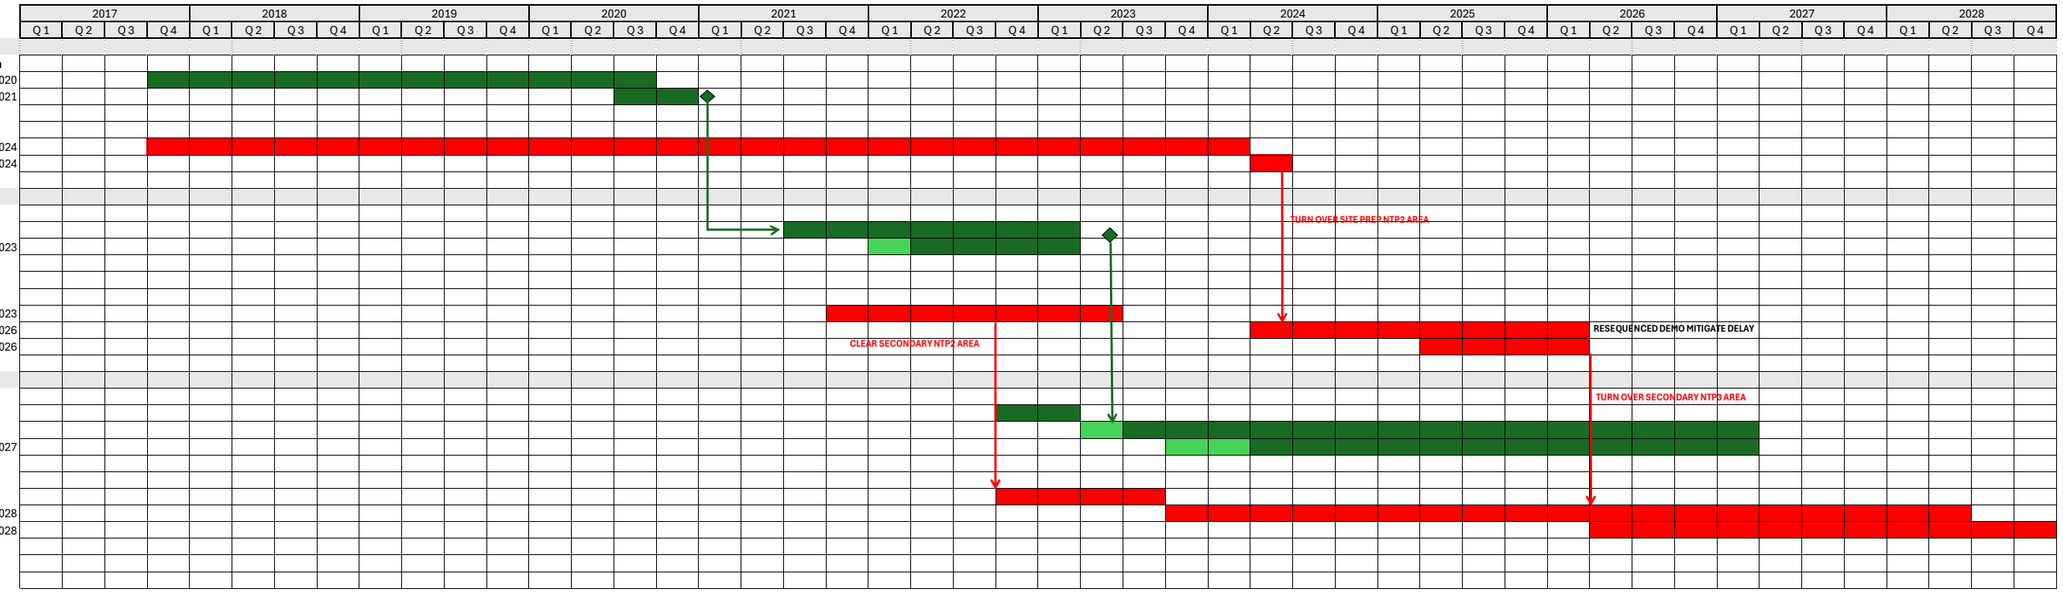
	Start	Finish
Primary Treatment Facility		
Contract		
NTP2 - Milestone B - Process Operation	12/1/2017	7/15/2020
Substantial Completeion - Decommissioning and Demo	7/16/2020	1/25/2021
Actual		
NTP2 - Milestone B - Process Operation	12/1/2017	3/1/2024
Decommissioning and Demo	3/14/2024	5/1/2024
Site Preparation Project		
Contract		
NTP1 - Admin and Utility Relocation	9/8/2021	
NTP2 - Construction (Early Start 3/1/22)	6/1/2022	6/1/2023
(Starts with Demo of Existing Primary Facilty)		
Actual		
NTP1 - Admin and Utility Relocation	9/30/2021	6/1/2023
NTP2 - Demo Primary and Maintenance Bld	6/3/2024	1/12/2026
NTP2 - Demo Primary Control Building	5/1/2025	1/30/2026
Secondary and Thickening/Dewatering Project		
Contract		
NTP1 - Admin	11/1/2022	
NTP2 - Secondary (Early Start 4/1/23)	7/1/2023	
NTP3 - Thickening and Dewatering (Early Start 12/1/23)	4/1/2024	2/22/2027
Actual (Rev. Baseline)		
NTP1 - Admin	12/1/2022	
NTP2 - Secondary (Early Start 4/1/23)	12/4/2023	5/26/2028
NTP3 - Thickening and Dewatering (Early Start 12/1/23)	2/2/2026	12/21/2028
